



ID	Task Name	Duration	Start	Finish	Predecess	28, '09	Jul 5, '09	Jul 12, '09	Jul 19, '09	Jul 26, '09	Aug 2, '09	Au
						T	TFSSMT	TFSSMT	TFSSMT	TFSSMT	TFSSMT	TFSSMT
1	Rifle Fire Station #3	171 days?	Thu 7/2/09	Thu 2/25/10								
2	Notice to Proceed	0 days	Thu 7/2/09	Thu 7/2/09								
3	Long Lead Procurement	24 days	Thu 7/2/09	Tue 8/4/09								
4	S.S. & J/D Package	10 days	Thu 7/2/09	Wed 7/15/09	2							
5	Mech. Units	20 days	Wed 7/8/09	Tue 8/4/09	2							
6	Cold Rolled Trusses	20 days	Wed 7/8/09	Tue 8/4/09	2							
7	Shop Drawings	39 days	Thu 7/2/09	Tue 8/25/09								
8	Rebar	10 days	Thu 7/2/09	Wed 7/15/09	2							
9	Structural Steel / Joist & Deck	11 days	Thu 7/16/09	Thu 7/30/09	4							
10	Truss System	15 days	Wed 8/5/09	Tue 8/25/09	6							
11	Concrete Designs	5 days	Thu 7/16/09	Wed 7/22/09	8							
12	Mass Excavation	5 days	Thu 7/2/09	Wed 7/8/09								
13	Bench Out to 100'	5 days	Thu 7/2/09	Wed 7/8/09	2							
14	Building Foundation Dig	10 days	Thu 7/9/09	Wed 7/22/09								
15	App Bay	3 days	Thu 7/9/09	Mon 7/13/09	13							
16	Office Area	7 days	Tue 7/14/09	Wed 7/22/09	15							
17	Pour Foundation	5 days	Thu 7/23/09	Wed 7/29/09	11							
18	App Bay	5 days	Thu 7/23/09	Wed 7/29/09	15							
19	Office Area	5 days	Thu 7/23/09	Wed 7/29/09	16							
20	Backfill	15 days	Thu 7/30/09	Wed 8/19/09								
21	App Bay	10 days	Thu 7/30/09	Wed 8/12/09	19							
22	Office Area	5 days	Thu 8/13/09	Wed 8/19/09	21							
23	Underslab Utilities	10 days	Thu 8/6/09	Wed 8/19/09								
24	App Bay	5 days	Thu 8/6/09	Wed 8/12/09	21FS-5 da							
25	Office Area	5 days	Thu 8/13/09	Wed 8/19/09	22FS-5 da							
26	SOG Prep	10 days	Thu 8/13/09	Wed 8/26/09								
27	SOG Prep	5 days	Thu 8/13/09	Wed 8/19/09	24							
28	SOG Pour	5 days	Thu 8/20/09	Wed 8/26/09	27							
29	Masonry	50 days	Thu 8/20/09	Wed 10/28/09								
30	Structural masonry	30 days	Thu 8/20/09	Wed 9/30/09	28FS-5 da							
31	Veneer	20 days	Thu 10/1/09	Wed 10/28/09	30							
32	Steel Erection	22 days?	Thu 10/1/09	Fri 10/30/09	9							
33	Delivery to site	1 day?	Thu 10/1/09	Thu 10/1/09	30							
34	Erection	21 days	Fri 10/2/09	Fri 10/30/09	33							
35	Structural Framing	30 days	Thu 8/27/09	Wed 10/7/09	10							
36	Frame Walls	20 days	Thu 8/27/09	Wed 9/23/09								
37	Set Cold Rolled Trusses	10 days	Thu 9/24/09	Wed 10/7/09	36							
38	OSB Sheathing	4 days	Thu 10/1/09	Tue 10/6/09	37FS-5 da							
39	Roofing	19 days	Thu 10/1/09	Tue 10/27/09								

Project: Rifle fire #3 Master Date: Thu 8/27/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	28, '09	Jul 5, '09	Jul 12, '09	Jul 19, '09	Jul 26, '09	Aug 2, '09	Au
						T	T	T	T	T	T	T
40	Standing Seam Roofing and Insulation	15 days	Wed 10/7/09	Tue 10/27/09	38							
41	EPDM Roofing and insulation	15 days	Thu 10/1/09	Wed 10/21/09	30							
42	MEP Rough	29 days	Thu 10/15/09	Tue 11/24/09	5							
43	Mechanical	15 days	Thu 10/15/09	Wed 11/4/09	41FS-5 da							
44	Electrical	15 days	Wed 10/21/09	Tue 11/10/09	40FS-5 da							
45	Plumbing	15 days	Wed 11/4/09	Tue 11/24/09	44FS-5 da							
46	Drywall	35 days	Wed 11/25/09	Tue 1/12/10								
47	Insulate	10 days	Wed 11/25/09	Tue 12/8/09	45							
48	Tape&Finish	10 days	Wed 12/2/09	Tue 12/15/09	47FS-5 da							
49	Paint	20 days	Wed 12/16/09	Tue 1/12/10	48							
50	MEP Trim	15 days	Wed 1/13/10	Tue 2/2/10								
51	Casework	15 days	Wed 1/13/10	Tue 2/2/10	49							
52	Interior Finishes	15 days	Wed 1/13/10	Tue 2/2/10	49							
53	Punchlist	17 days?	Wed 2/3/10	Thu 2/25/10								
54	Final Clean	10 days	Wed 2/3/10	Tue 2/16/10	52							
55	Substantial Completion	1 day?	Wed 2/17/10	Wed 2/17/10	54							
56	Arch/Owner punch	3 days	Thu 2/18/10	Mon 2/22/10	55							
57	Final Inspections	2 days	Tue 2/23/10	Wed 2/24/10	56							
58	Final C. O.	1 day?	Thu 2/25/10	Thu 2/25/10	57							




Project: Rifle fire #3 Master Date: Thu 8/27/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

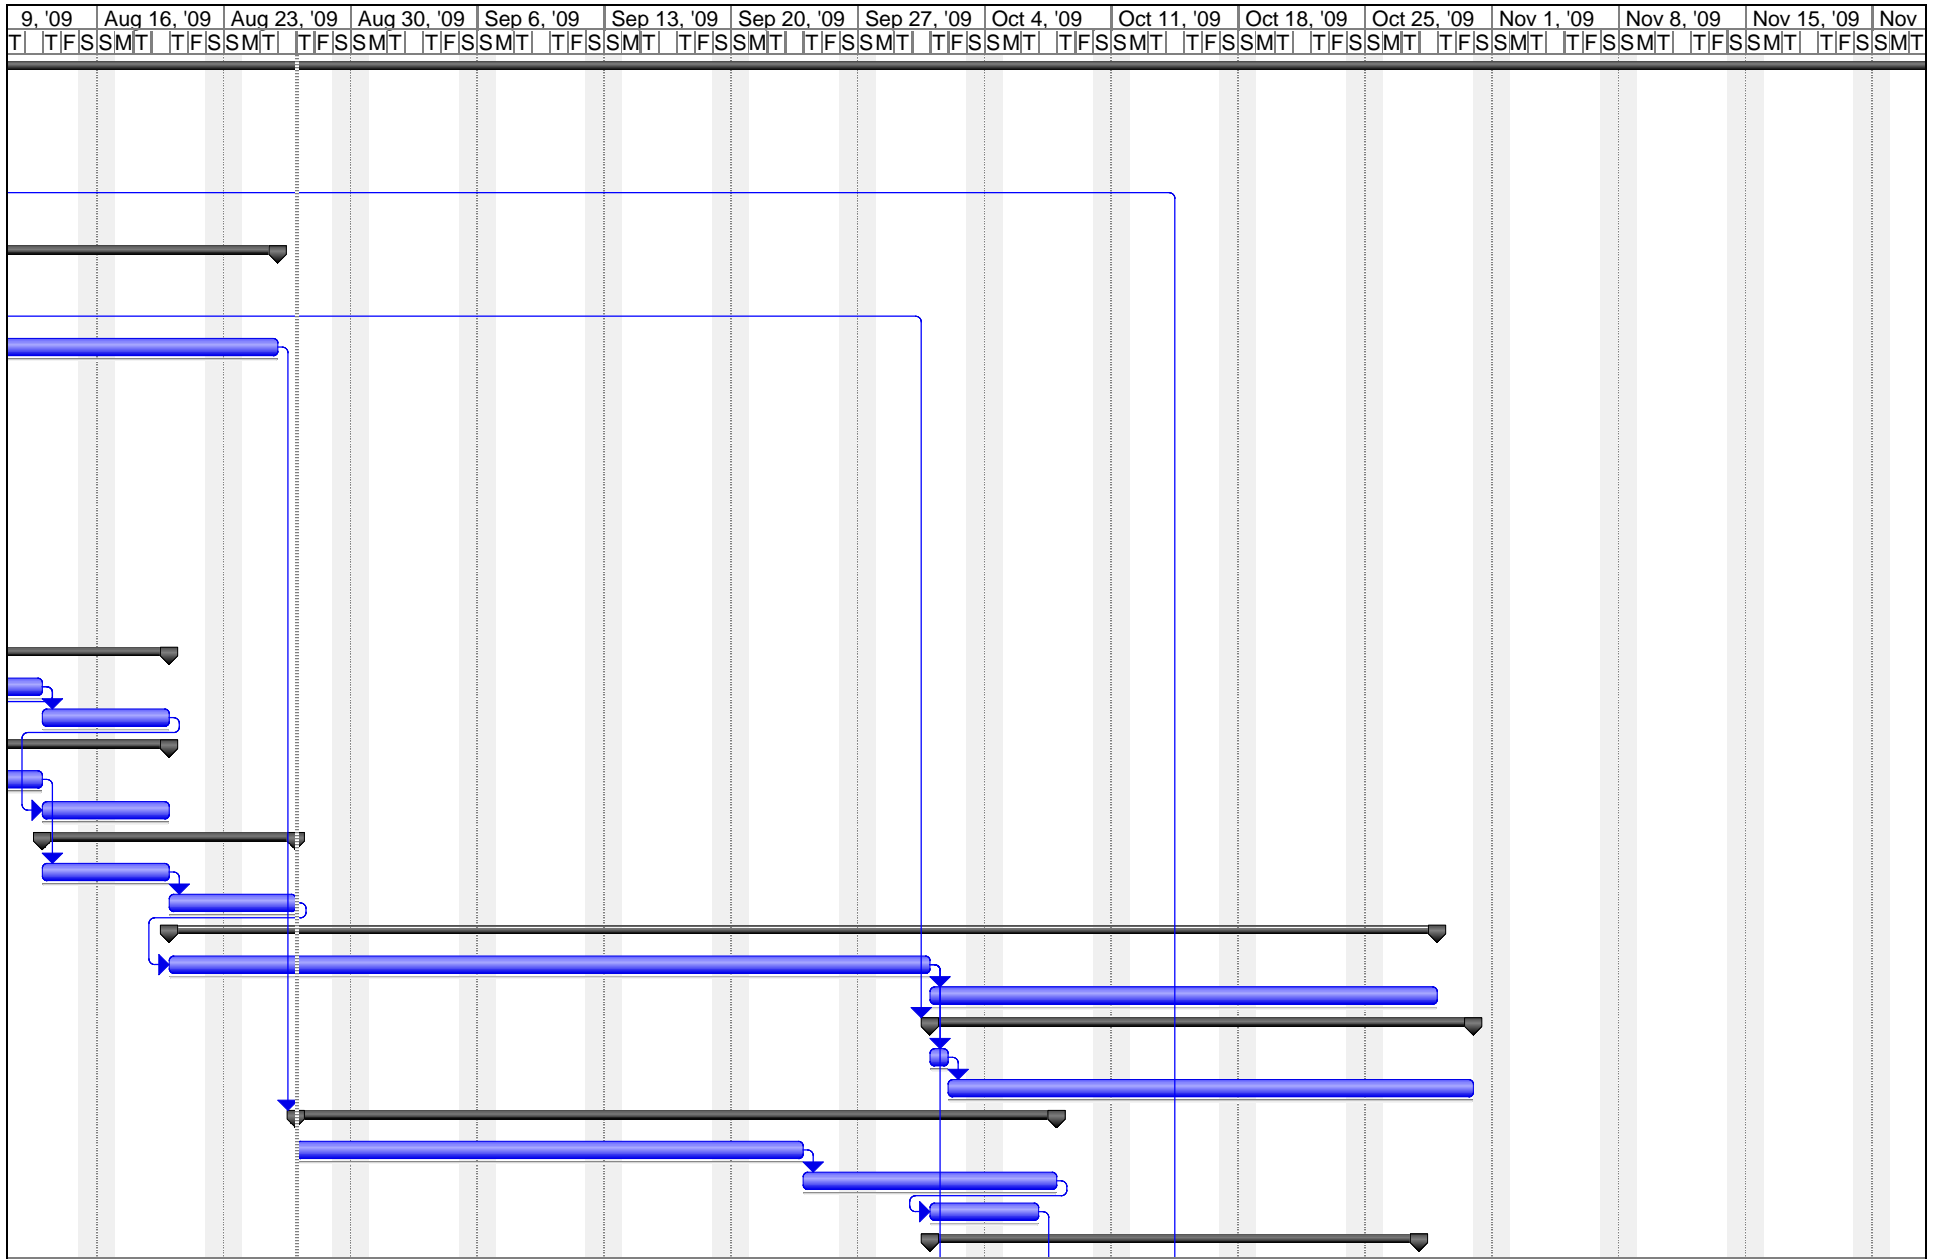


Project: Rifle fire #3 Master
 Date: Thu 8/27/09



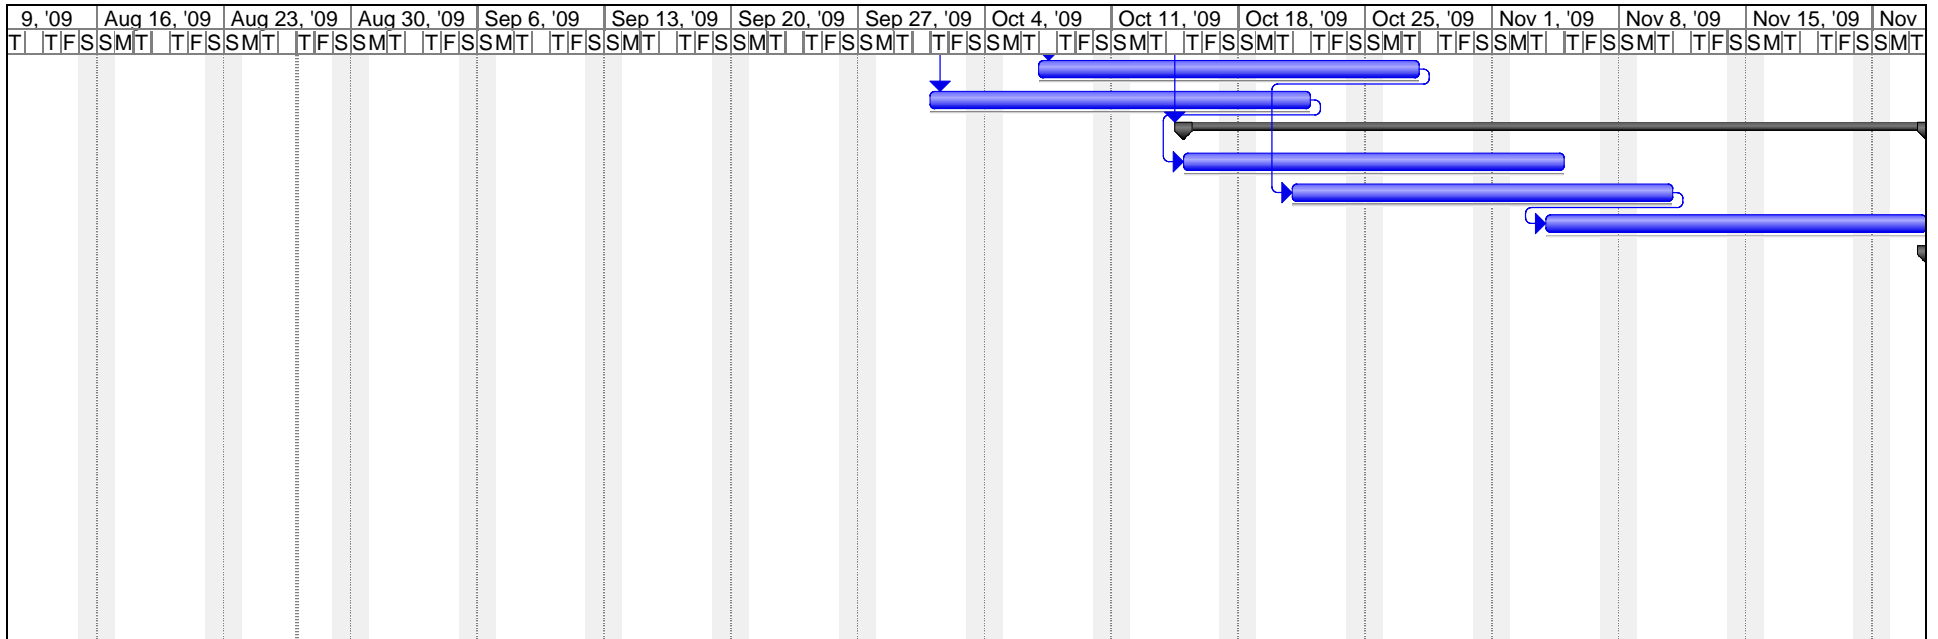






Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Project: Rifle fire #3 Master
Date: Thu 8/27/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Project: Rifle fire #3 Master Date: Thu 8/27/09	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

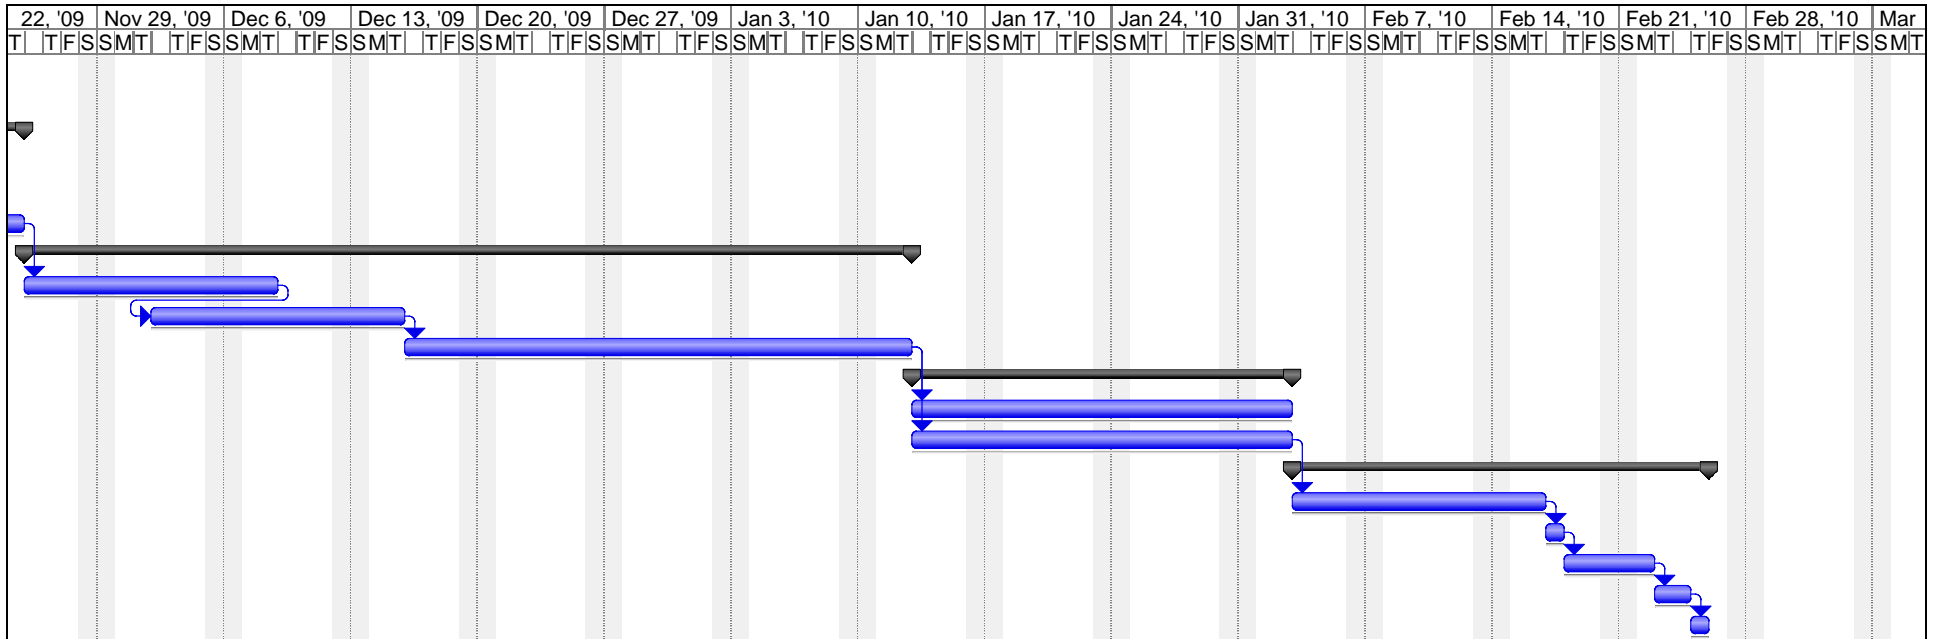

Project: Rifle fire #3 Master Date: Thu 8/27/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
